


ECT steps (Nov)




C


A

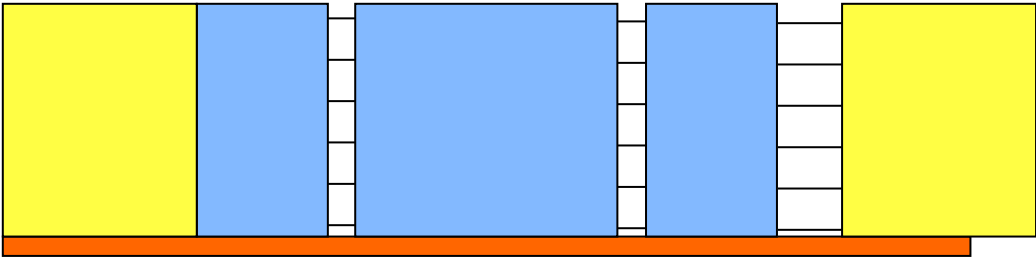

Today

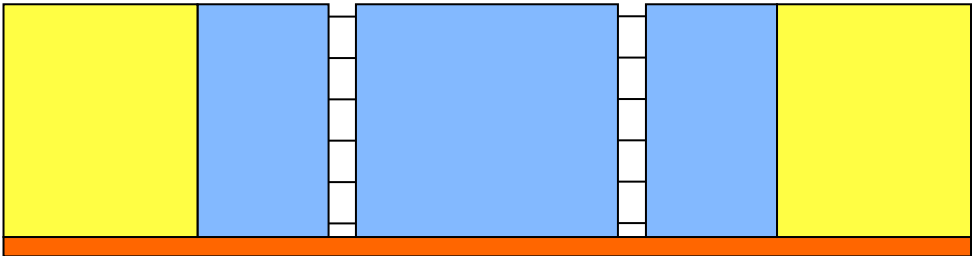

Just before ECT test
(week 45, 7 November)

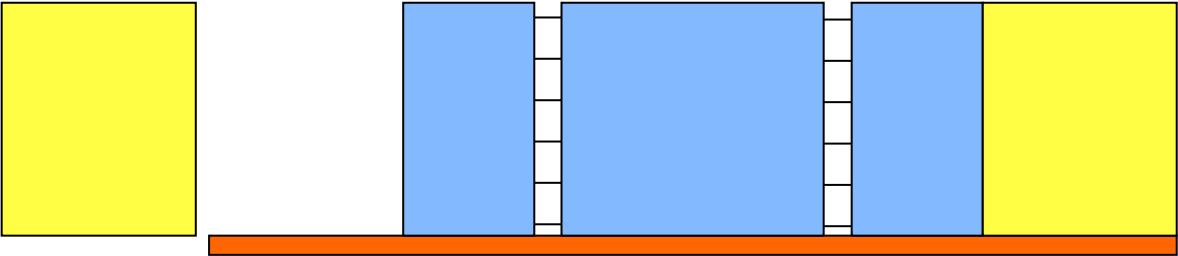


As soon ECTC tested
(28-29 November)

CALO/SW steps (Dec)




C

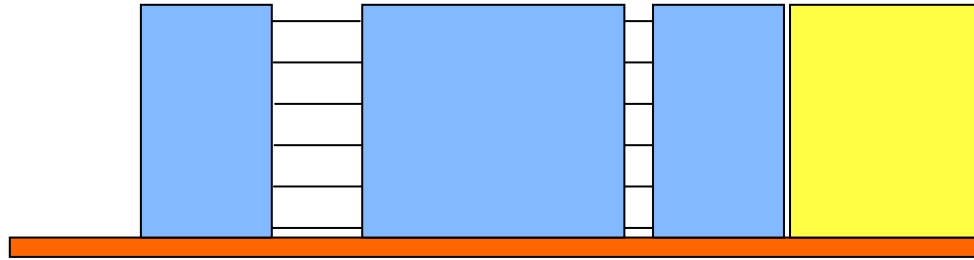

A

As soon ECT-C on truck, then move calo-C to 3m aperture (week 49, by the 7th of December ok)

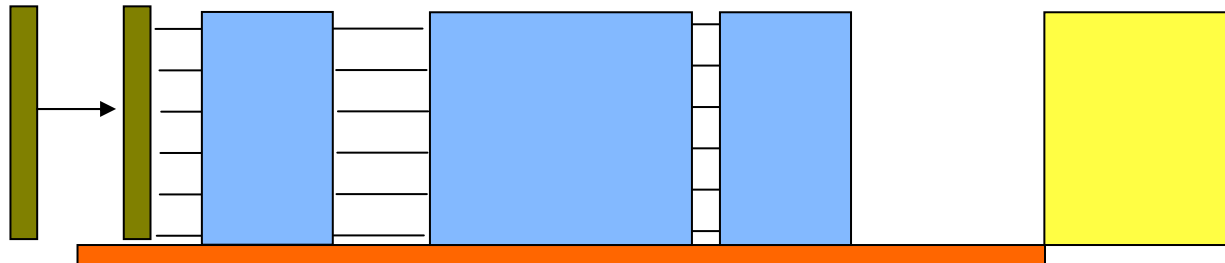


As soon SWC ready, lower it down, the week before Xmass. Also open ECT-A


This mean:

1. EO A has more time, probably until mid December to install all structures on side A. Side C EO might be already finished.
2. EBC is 3m open, refurbishing can start the second week of December on side C. Pixel can also start on side C then. On side A the pixel can progress until Xmas
3. SW in place side C, connection can start end of December

SW steps (Jan)

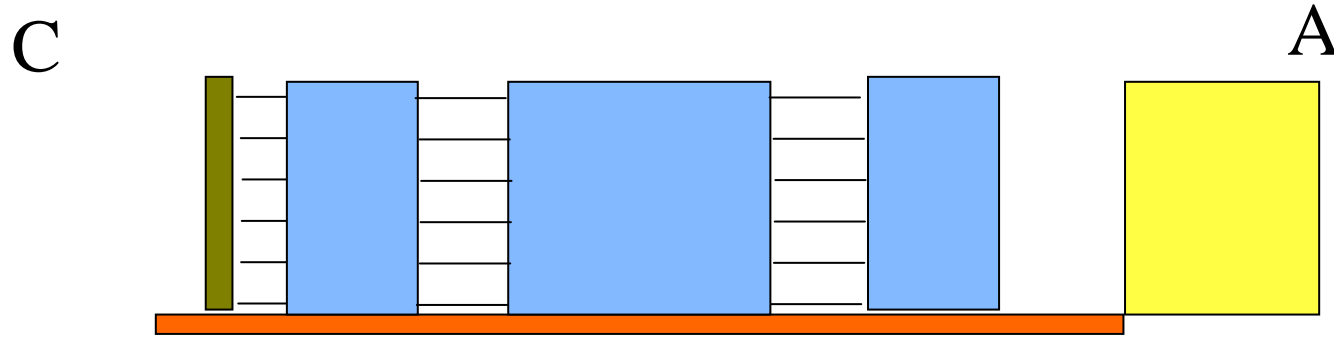

Move calo-A to 3m aperture
(week 2, when ID manpower
not available)


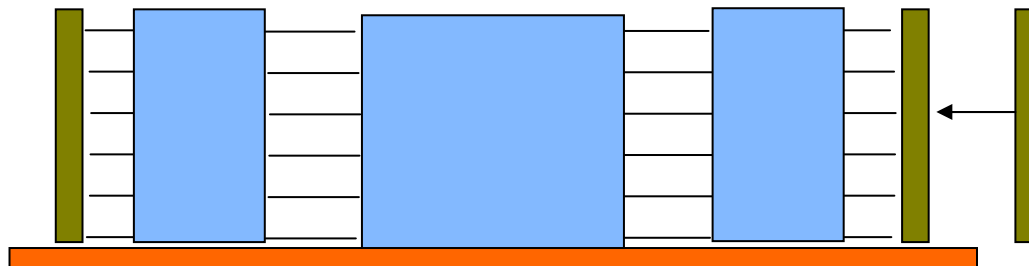


As soon SWA ready,
lower it down, mid
January


This mean:

1. EBA is 3m open, refurbishing can start the 3 week of January on side A. Pixel can also continue on side A
2. SW in place side A, connection can start the last week of January

Closing steps (from end Feb)

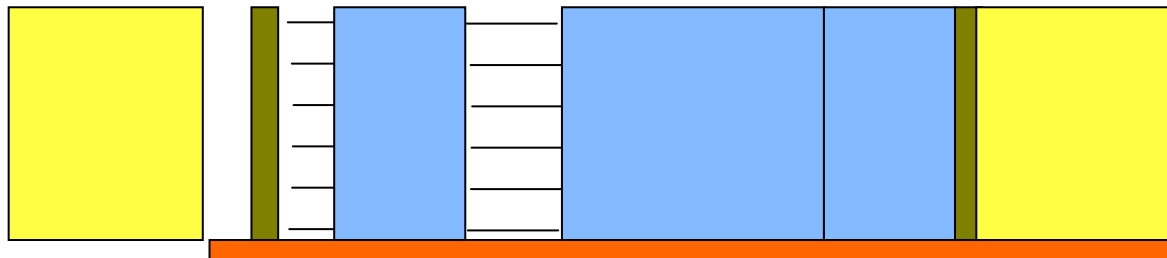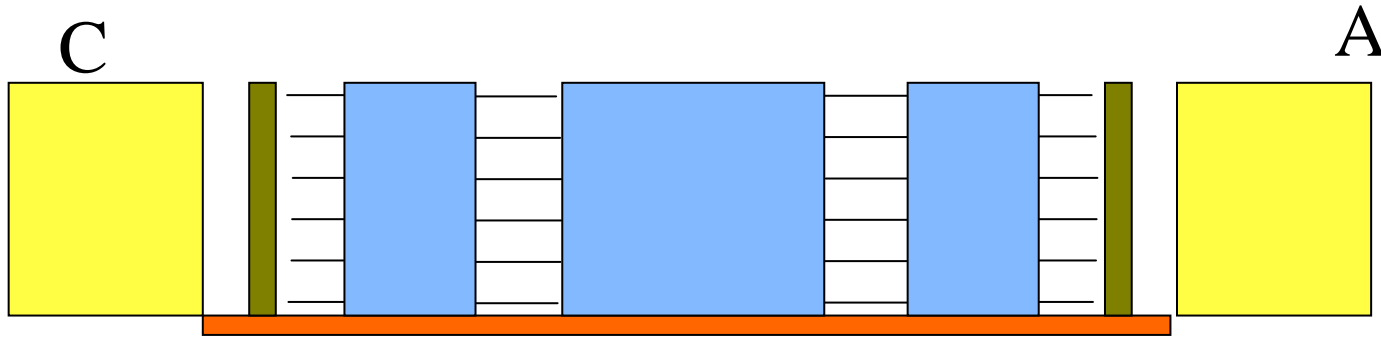

As soon ID A and Calo A sign off (week 12, 21st March), Close pipe side A + JF shielding (week 14)

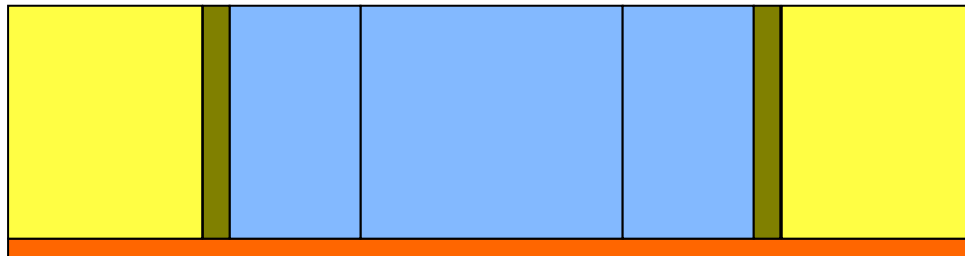

As soon ID C and Calo C sign off (week 13), Magnet test can just start in April. Close pipe side C +JF shielding (week 15, mid April)
